



Shasta College

Measure H Projects Update

As of 10/17/2018

Regional Public Safety Training Center



Project Start:
6/2018

Est. Completion:
12/2018



NICHOLS
MELBURG
ROSSETTO
ARCHITECTS / ENGINEERS

ARCHITECT



GIFFORD CONSTRUCTION, INC.
— Established 1972 —
CALIFORNIA LICENSE NO. 638891

CONTRACTOR



Regional Public Safety Training Center



Athletic Fieldhouse with Restrooms



Project Start:

8/2018

Est. Completion:

2/2019



NICHOLS
MELBURG
ROSSETTO
ARCHITECTS / ENGINEERS

ARCHITECT

Cerami & Browning
CONSTRUCTION, INC.

CONTRACTOR



Gymnasium Air Conditioning

Project Start:
10/2018

Est. Completion:
1/2019



NICHOLS
MELBURG
ROSSETTO
ARCHITECTS / ENGINEERS


ARCHITECT

Cerami & Browning
CONSTRUCTION, INC.

CONTRACTOR



Solar Project – East Lot

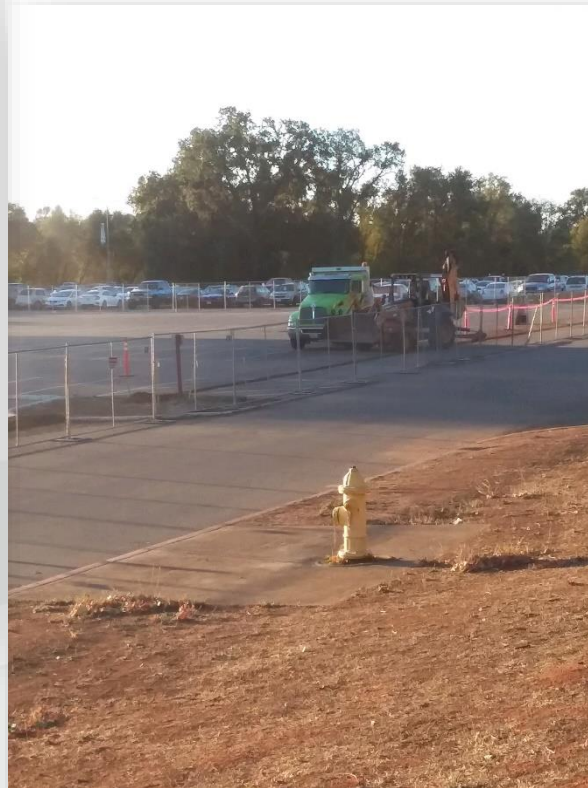

Project Start:
10/2018

Est. Completion:
6/2019



NICHOLS
MELBURG
ROSSETTO
ARCHITECTS / ENGINEERS

ARCHITECT

SUNPOWER®

CONTRACTOR



Approval Received

Construction Commenced/To Commence:

- Regional Public Safety Training Center – Phase One (recommenced 9/10/18)
 - Gifford Construction, Inc. (Infrastructure) and Trent Construction (Props)
 - Props to be delivered 10/23/18 and 10/30/18
- Athletic Fieldhouse with Restrooms
 - Cerami & Browning Construction, Inc. (commenced 8/27/18)
- Gymnasium Air Conditioning
 - Cerami & Browning Construction, Inc. (commenced 10/8/18)
- Solar Project – East Lot
 - Sunpower (commenced 10/8/18)

In Bid Process:

- Campus Safety Relocation – Interior remodel (Out to bid – Closes 10/30/18)





Projects Update (continued)

Under DSA Review

- Veterans Center Building
- CTE Building and Covered Storage
- Regional Public Safety Training Center Classroom Buildings

DSA Submission Pending

- Tehama Campus Student Services Building (to DSA late October)

Design Phase

- CIS Building



Non-DSA Projects

Current/Upcoming Projects

- 2400 Building – Electrical Upgrade (COMPLETED)
- HSUC Folding Wall Replacement
 - Bid documents being prepared
- SC Main Campus Keying & Access Control
 - Ongoing construction document preparation
- SC Safety & Security Standards
 - In Progress
- Campus Wide Infrastructure Projects (water, sewer, storm drain, electrical, fire alarm, technology fiber, gas lines)
 - Report of CCTV scoping of sewer system/storm drains forthcoming



For more information...

About SC / Bond Information / 2016 Bond Measure H



tmarkword@shastacollege.edu / 242-7699

Theresa Markword, Bond Program Manager

