



Shasta College

Measure H Bond Projects & Capital Construction Update

Presented to the
Shasta College Counseling Team
9/25/2024



Completed Projects

\$143 Million in Completed and Ongoing Projects
throughout the District

Completed projects related to Student Services:



Tehama Campus
Student Services Center
TOTAL COST: \$6,121,902

Veterans Support
and Success Center
TOTAL COST: \$2,692,752



Completed Projects *(continued)*

Regional Public Safety Training Center – Phase 1



BURN TOWER

TOTAL COST: \$2,869,310

RAPPELLING TOWER



Completed Projects *(continued)*

Career Technical Educational Building & Covered Storage



TOTAL COST: \$5,288,645



Completed Projects *(continued)*

Computer Information Systems (CIS) Building



TOTAL COST: \$8,319,255



Completed Projects *(continued)*

Solar Array – East Parking Lot



TOTAL COST: \$6,900,000



Completed Projects *(continued)*

SC Community Leadership Center



TOTAL COST: \$22,742,950
(New Markets Tax Credits Offset
= \$4.1 Million)



Projects Under Construction



Library Interior
Circulation Desk Area



Raised Planters /Student Seating
At Entry Plaza

Library Building coming online in Fall 2025

- Tutoring & Learning Center
- Quiet Study Area (Stacks)
- Open Computer Lab
- Library Instruction Classroom
- 12 Student Study Rooms
- Gaming Room
- 4 Conference Rooms
- General Instruction Classroom (Upstairs)
- Center for Excellence
- Staff Lounge with Balcony Seating
- Administrative Offices
- Research, Ed Tech & Early College



Projects Under Construction *(continued)*



1400-1600 Buildings
Shade Structure Project




Project Timelines

Project Name	Status	Start Const	End Const
200 Building (Library) Renovation	Under Construction	6/1/2023	3/31/2025
1400-1600 Buildings Shade Structures & Fire Lane	Under Construction	7/8/2024	10/15/2024
5200 Building (CAL FIRE Locker Rooms)	Under Construction	9/16/2024	3/31/2025
SC Main Campus Electrical Wire Replacement	Future Construction	12/24/2024	3/31/2025
2300 Building (Bookstore) Renovation	Future Construction	12/16/2024	4/30/2025
SC Main Campus Quad Project	Future Construction	5/19/2025	8/14/2025
800 Building (Instructional Classrooms) Renovation	Future Construction (HazMat Abatement Complete)	12/2/2024	3/31/2026
700 Building (Administrative Offices) Renovatoin	Future Construction	6/2/2025	6/1/2026
6-Story Fire Tower (SC Fire Academy)	Future Construction	7/1/2025	7/31/2026
Apparatus Bay (CAL FIRE)	Future Construction	9/1/2025	12/31/2026
Fueling Station	Future Construction	9/1/2025	12/31/2026
100 Building Renovation	Future Construction	11/2/2026	5/1/2028
Space Refresh - Interior/Exterior	Future Construction	Ongoing	

*** Planned power outage from 12/24/24 – 1/3/25 ***



Campus Navigation

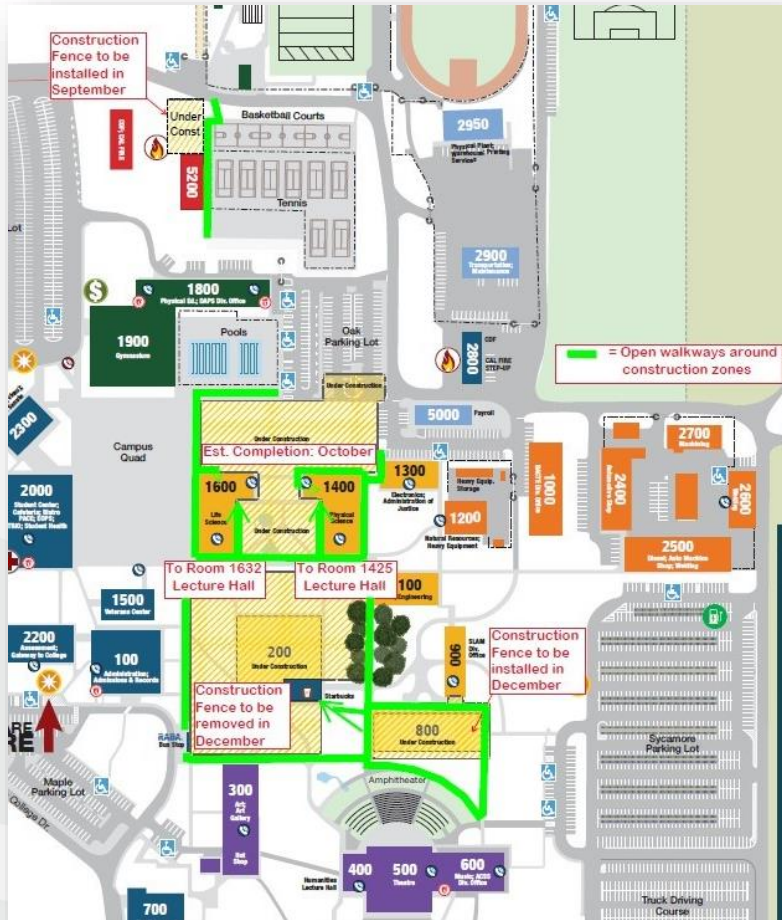

Updated Navigation Map will be Available in December



Upcoming Department/Staff Moves




Spring/Summer 2025 Moves

- 1 – Library Services / Tutoring & Learning Ctr from 700 to 200
- 2 – Library Staff & Library Books from 2200 to 200
- 3 – Student Services from 100 to 2100
- 4 – Student Services from 100 to 2300
- 5 – Technology from 700 to 100




2100 Building Student Services Functions

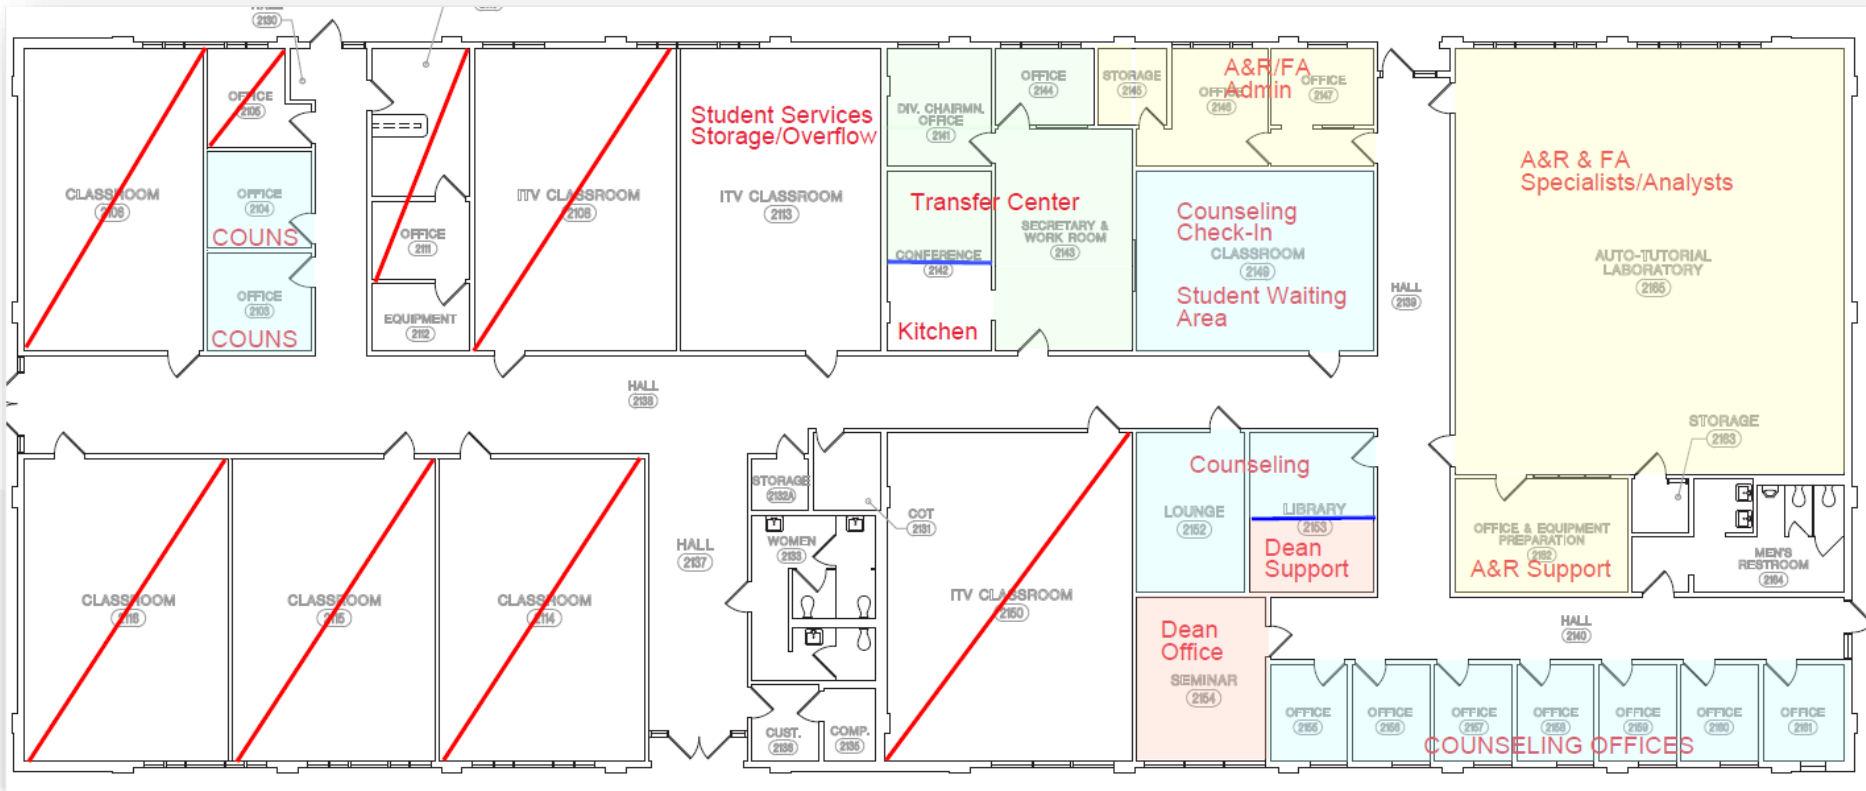

Space refreshes will begin after the accreditation visit next week.



Bookstore Renovation

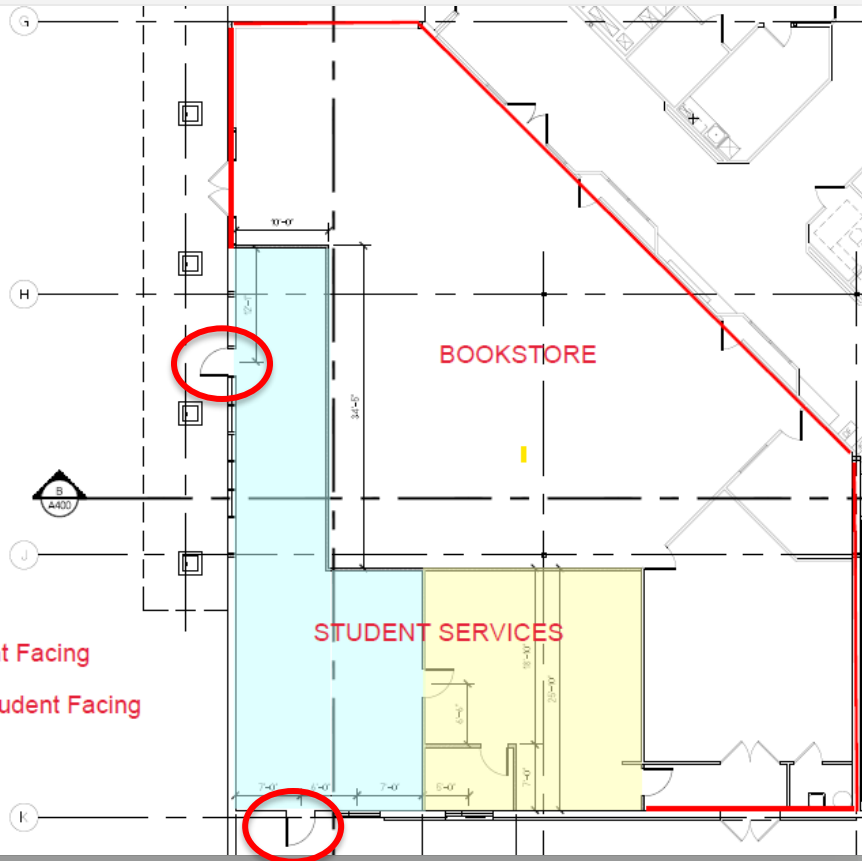

Student Services

2100 Building Functions:

- Counseling
- Transfer Center
- A&R and Financial Aid Specialists (non-student facing)
- Dean's Office


Student Services

2300 Building Functions:

- Registration
- Financial Aid
- Student Success Center



Signage & Navigation

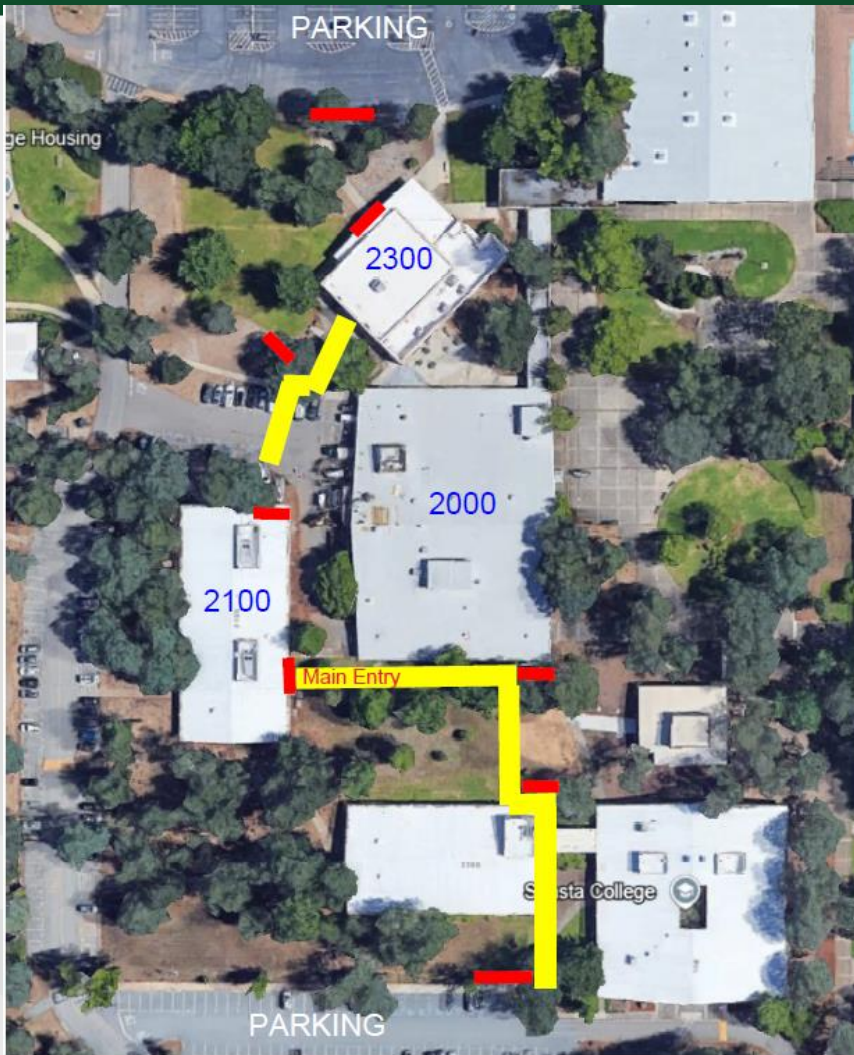

How will students find us??

— = Signage

— = Route

- Direct students to 2100 Main Entry
- New Signage on 100 Building for A&R and Counseling will be moved to 2100



SC Main Campus Student Services Building



ESTIMATED TOTAL COST: \$10,500,000



SC Main Campus Student Services Building *(continued)*



SC Main Campus Student Services Building *(continued)*




SC Main Campus Student Services Building *(continued)*



SC Main Campus Student Services Building *(continued)*



SC Main Campus Student Services Building *(continued)*

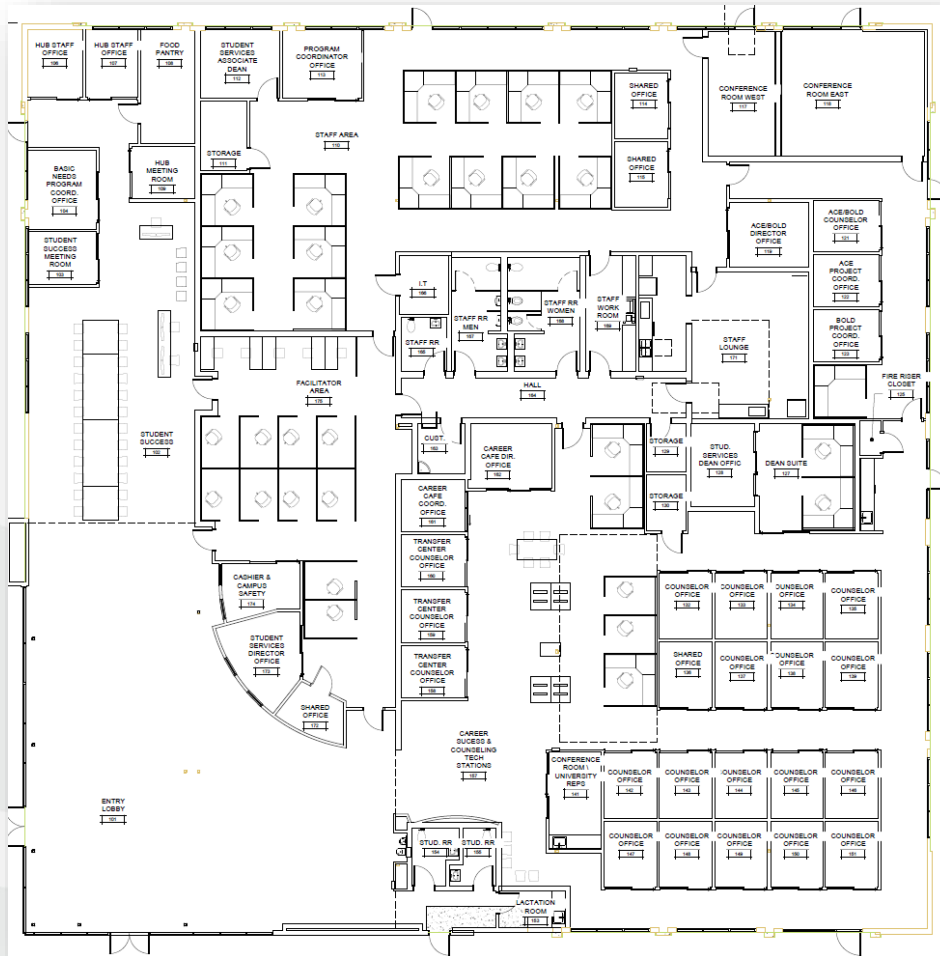

- DRAFT Floor Plan
- Revisions possible based upon Division of the State Architect comments



QUESTIONS

*Thank
you!*



For more information...



About / Bond Projects / Measure H



Theresa Markword,
Interim AVP of Facilities &
Capital Construction
tmarkword@shastacollege.edu
(530) 242-7699

Sherry Nicholas,
Bond Program Project Coordinator
snicholas@shastacollege.edu
(530) 242-7527

Isabella Greenleaf,
Bond Program Project Coordinator
igreenleaf@shastacollege.edu
(530) 242-7978

Magan Kleinman,
Bond Program Administrative Secretary II
mkleinman@shastacollege.edu
(530) 242-7747

